

**Acuren Group Inc.**

2 - 240 Taiganova Crescent
Fort McMurray, AB, Canada T9K 0T4
www.acuren.com

Phone: 780.790.1776
Fax: 780.790.9061

Page 1 of 4

A Higher Level of Reliability

NONDESTRUCTIVE EXAMINATION

CLIENT: **Suncor Energy Inc.**
Suncor Oil Sands
Fort McMurray, AB

DATE: February 27, 2026

ACUREN JOB #: 272-J280794

REPORT #: **UT-BALJIN-2026-15**

CONTRACT/PO: SUENTQ00169932 WO: 300655037

WORK LOCATION: Plant 57

ATTENTION: **Condition Monitoring Group**

PROJECT: Corrosion 2026

ITEM(S) EXAMINED: **CML 2.30**

PART #: See results MATERIAL: Carbon Steel THICKNESS: Various

SCOPE: Perform UT thickness scans as per request.

TYPE OF INSPECTION: Ultrasonic

TEST DETAILS:

ACCEPTANCE STANDARD: Client's information

REVISION: N/A

PROCEDURE/TECHNIQUE: CAN-UT-14T001

REVISION: 12

TYPE: Thickness

METHOD: Contact

INSTRUMENT: Olympus

MODEL: 38 DL Plus

S/N: 173091112

CAL DUE: July 24 2026

CAL. BLOCK: Step block

S/N:

CABLE-TYPE: Coaxial

LENGTH: 5ft

CAL. BLOCK: Step block

S/N: **17-1028 CS**

COUPLANT: Sono600

Probe & Technique Details:

	TEST ANGLE (°)	PROBE TYPE	CRYSTAL SIZE	FREQ. (MHZ)	SERIAL NUMBER	DAMPING Ω	TEST FROM	REFERENCE REFLECTOR	TRANSFER VALUE	REFERENCE		SCAN dB	RANGE
										dB	% FSH		
1	0	D799	3/8"	5	1566949	N/A	OD	Backwall	0	65	80	N/A	5.00"
2													
3													
4													

TEST SURFACE CONDITION: Rough

TEST SURFACE TEMPERATURE: **50°F**

RESULTS:

Circuit:
57-034B 4-4
CML
2.30

Client acknowledges receipt and custody of the report or other work ("Deliverable"). Client agrees that it is responsible for assuring that acceptance standards, specifications and criteria in the Deliverable and Statement of Work ("SOW") are correct. Client acknowledges that Acuren is providing the Deliverable according to the SOW, and not any other standards. Client acknowledges that it is responsible for the failure of any items inspected to meet standards, and for remediation. Client has 15 business days following the date Acuren provides the Deliverable to inspect it, identify deficiencies in writing, and provide written rejection, or else the Deliverable will be deemed accepted. The Deliverable and other services provided by Acuren are governed by a Master Services Agreement ("MSA"). If the parties have not entered into an MSA, then the Deliverable and services are governed by the SOW and the "Acuren Standard Service Terms" (www.acuren.com/service/terms) in effect when the services were ordered.

CLIENT:

CLIENT PRINTED NAME

CLIENT SIGNATURE

ACCEPTED & ACKNOWLEDGED BY

ACUREN

TECHNICIAN:

Jineil Ballesteros

1st Technician CGSB UT1
CGSB Reg. #29240



2nd Technician
CGSB Reg. #


REVIEWER:

Joshua Robertson
#28293

DTR No.: N/A

(Generated Using: CAN-QUA-02F007 R10 - 01/01/2024)

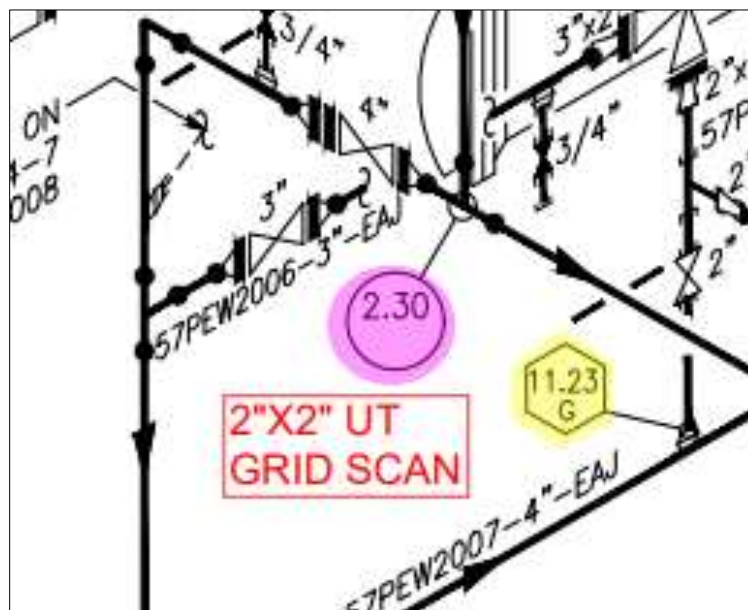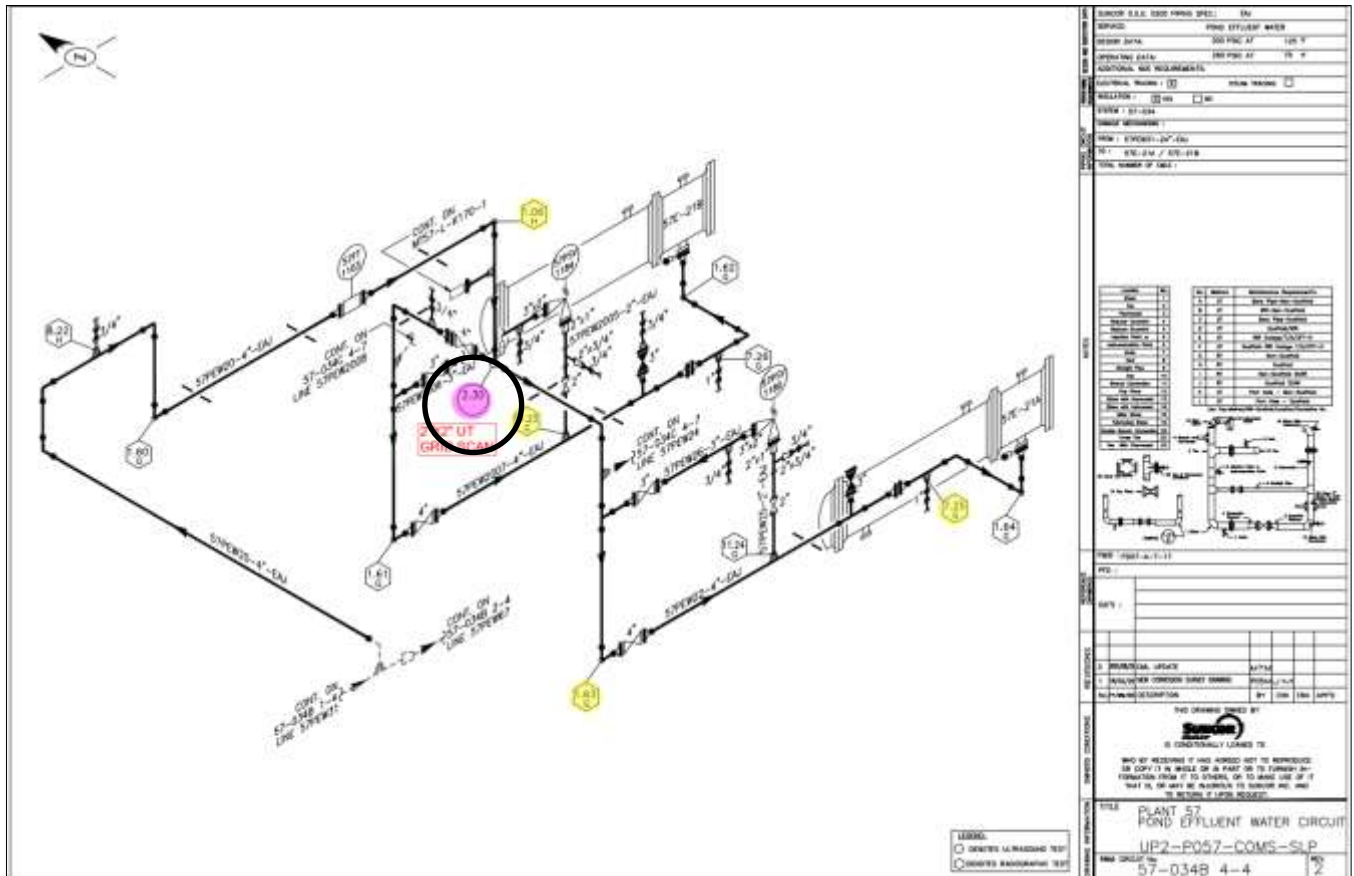

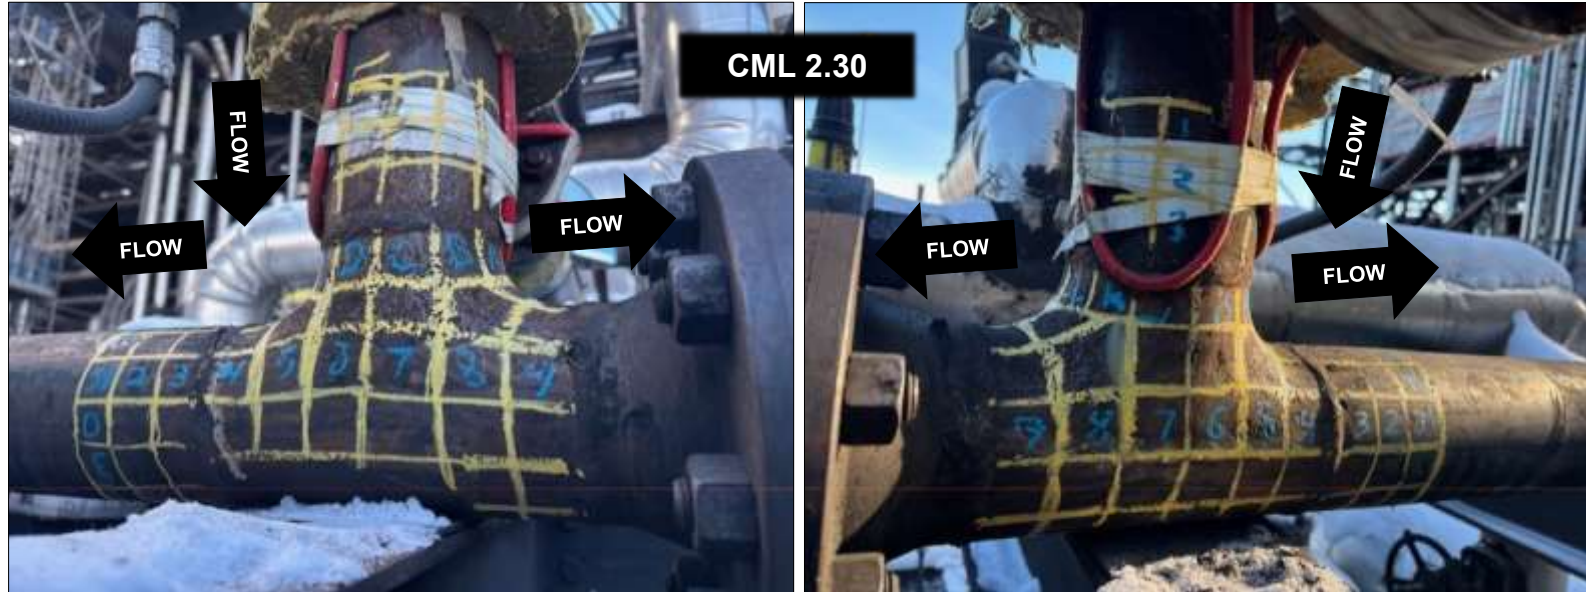

NOTE: 1"X1" GRID performed on **CML 2.30** starts at **TOP**. Letters **A – L** go around the with respect to flow. Numbers **1 – 9** goes with flow.
1"X1" GRID performed on **CML 2.30 TEE NECK** starts at **NORTH**. Letters **A – L** go around the with respect to flow. Numbers **1 – 4** goes with flow.
T.MIN under **0.125** located on Section 4.

CML 2.30													
1"X1"	A	B	C	D	E	F	G	H	I	J	K	L	
1	0.140	0.150	0.166	0.162	0.157	0.154	0.135	0.144	0.154	0.138	0.141	0.138	
2	0.134	0.145	0.157	0.156	0.162	0.142	0.143	0.142	0.158	0.143	0.138	0.145	
3	0.157	0.162	0.162	0.168	0.158	0.150	0.167	0.157	0.154	0.145	0.158	0.161	
WELD													
4	0.234	0.241	0.234	0.277	0.272	OBSTRUCTION			0.278	0.258	0.254	0.273	0.264
5	0.282	0.259	0.241	0.263	0.271				0.281	0.232	0.234	0.245	0.274
6	TEE NECK	0.221	0.237	0.217	0.293				0.283	0.186	0.088	0.158	TEE NECK
7		0.223	0.221	0.232	0.307	0.284	0.213	0.163	0.177				
8	0.277	0.265	0.259	0.227	0.257	0.305	0.273	0.289	0.226	0.300	0.245	0.240	
9	0.285	0.271	0.283	0.258	0.248	0.257	0.244	0.262	0.273	0.286	0.243	0.310	
CML 2.30 TEE NECK													
1"X1"	A	B	C	D	E	F	G	H	I	J	K	L	
1	0.206	0.192	0.185	0.196	0.206	0.189	0.168	0.187	TAPE	0.165	0.172	0.198	
2	0.197	0.188	0.190	0.180	0.181	0.189	0.182	0.193		0.202			
3	0.196	0.189	0.192	0.156	0.192	0.182	0.190	0.187		0.186	0.199	0.204	0.199
WELD													
4	0.238	0.168	0.169	0.162	0.184	0.246	0.254	0.194	0.204	0.209	0.243	0.267	

