Acuren Group Inc.
2 - 240 Taiganova Crescent
Fort McMurray, AB, Canada T9K 0T4
www.acuren.com
Phone: 780.790.1776
Fax: 780.790.9061

A Higher Level of Reliability

NONDESTRUCTIVE EXAMINATION

CLIENT: **Suncor Energy Inc.**
Suncor Oil Sands
Fort Mcmurray, AB

DATE: March 6, 2026
ACUREN JOB #: 272-J280794
REPORT #: UT-BALJIN-2026-28
CONTRACT/PO: SUENTQ00169932 WO: 300655876
WORK LOCATION: Plant 57

ATTENTION: **Condition Monitoring Group**
PROJECT: Corrosion 2026
ITEM(S) EXAMINED: **CML 1.04, 1.13**

PART #: See results MATERIAL: Carbon Steel THICKNESS: Various
SCOPE: Perform UT thickness scans as per request
TYPE OF INSPECTION: Ultrasonic

TEST DETAILS:

ACCEPTANCE STANDARD: Client's Information REVISION: N/A
PROCEDURE/TECHNIQUE: CAN-UT-14T001 REVISION: 12
TYPE: Thickness METHOD: Contact
INSTRUMENT: Olympus MODEL: 38 DL Plus S/N: 173091112 CAL DUE: July 24, 2026
CAL. BLOCK: Step Block S/N: **17-1028 CS** CABLE-TYPE: Coaxial LENGTH: 5ft
CAL. BLOCK: Step Block S/N: COUPLANT: Sonotech - Sono 600

Probe & Technique Details:

	Test Angle (°)	Probe Type	Crystal Size	Freq. (MHz)	Serial Number	Damping Ω	Test From	Reference Reflector	Transfer Value	Reference		Scan dB	Range
										dB	% FSH		
1													
2													
3	0	E58D1	3/8”	5	09027	N/A	OD	Backwall	0	65	80	N/A	2.00
4													

TEST SURFACE CONDITION: Bare TEST SURFACE TEMPERATURE: 240°F & 262°F

RESULTS:

Circuit:
57-001G 1-2
CML
1.04, 1.13

CLIENT: ____________ (CLIENT PRINTED NAME) ____________ (CLIENT SIGNATURE ACCEPTED & ACKNOWLEDGED BY)

DTR NO.: N/A

ACUREN TECHNICIAN: Jineil Ballesteros
1st Technician
CGSB 29240

2nd Technician
CGSB

REVIEWER: Narciso Jr Auteda
CGSB 30991

(Generated Using: CAN-QUA-02F007 R11 - 01/07/2026)

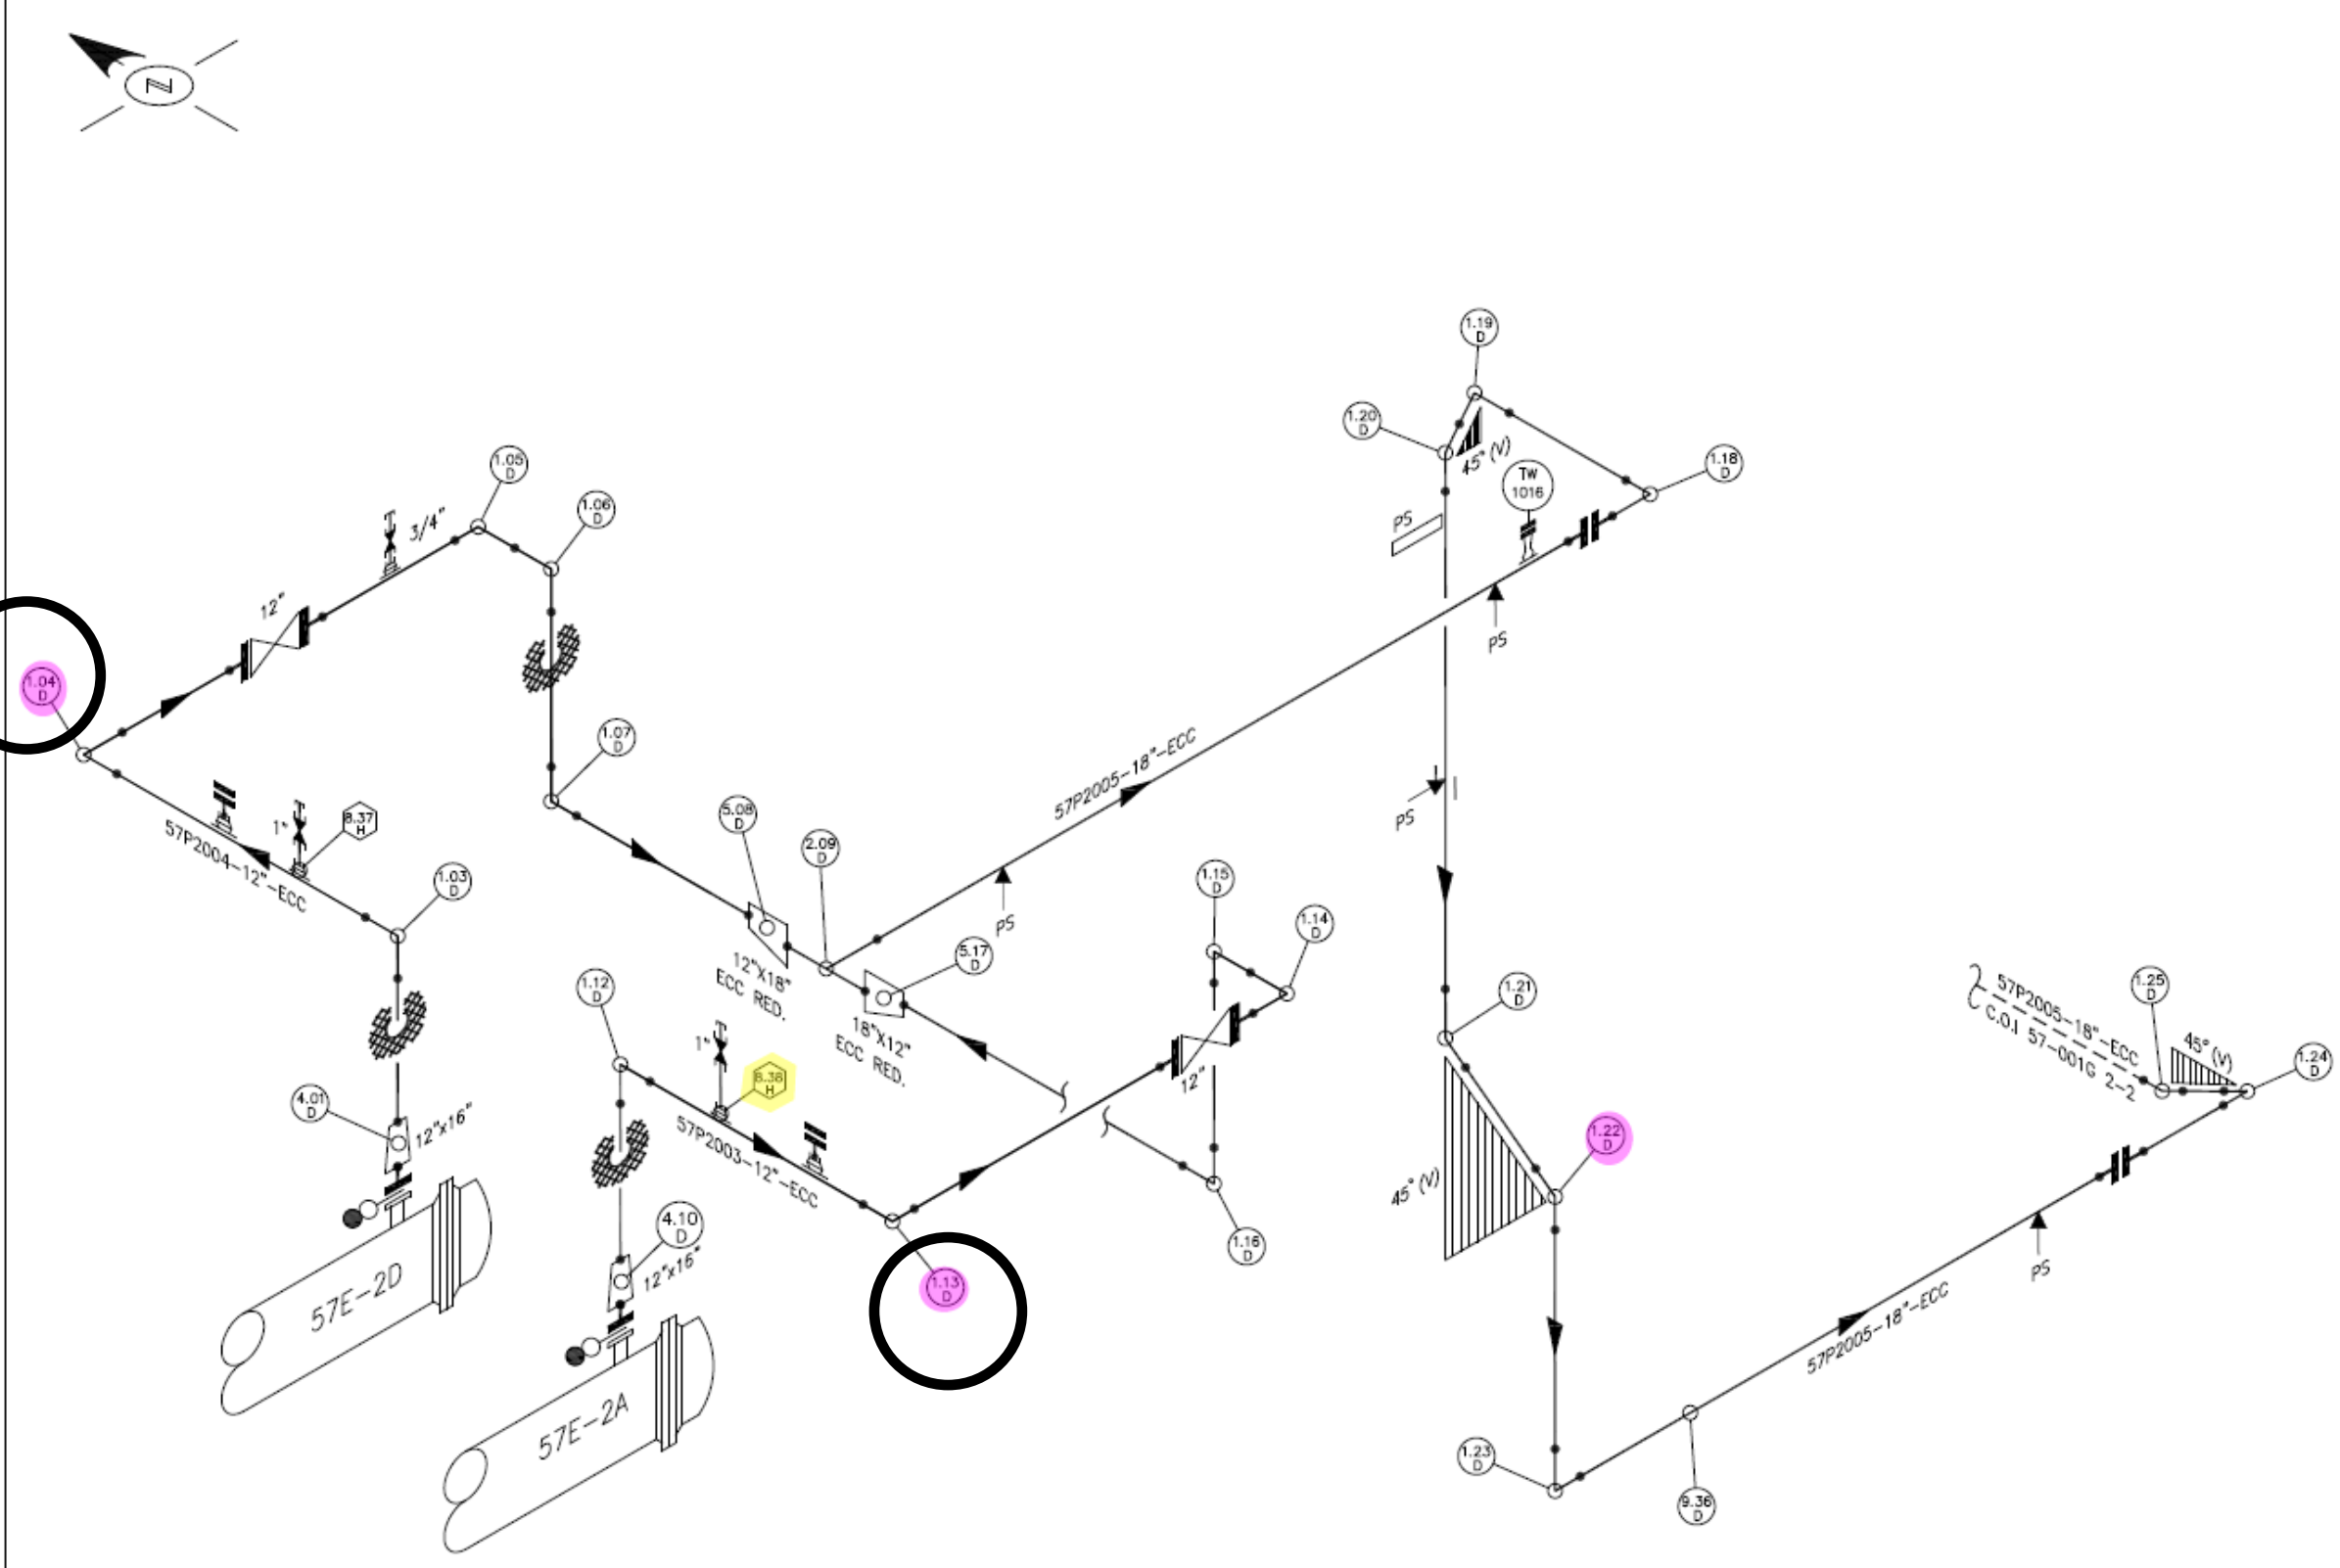

DESIGN AND INSPECTION DATA	SUNCOR O.S.G. 0200 PIPING SPEC.:
	SERVICE: DILUTED BITUMEN
	DESIGN DATA: 325 PSIG AT 350 °F
	OPERATING DATA: 70 PSIG AT 291 °F
	ADDITIONAL NDE REQUIREMENTS:
	ELECTRICAL TRACING : [X] STEAM TRACING: [ ]
	INSULATION : [X] YES [ ] NO
PIPING CIRCUIT INFORMATION	SYSTEM : 57-001
	DAMAGE MECHANISMS : MINERAL EROSION
	FROM :
	TO :
	TOTAL NUMBER OF CMLS :

NOTES

REFERENCE DRAWINGS AND EQUIPMENT

NOTE: -9.36 IS STRAIGHT SECTION DOWNSTREAM OF ELBOW
-UNLESS OTHERWISE SPECIFIED, ALL PIPES ARE INSULATED

Location	No.
Elbow	1
Tee	2
Thermowell	3
Reducer Conentric	4
Reducer Eccentric	5
Injection Point or	6
Instrumentation Point	6
Drain	7
Vent	8
Straight Pipe	9
Cap	10
Branch Connection	11
Pup Piece	12

No.	Method	Maintenance Requirement's
A	UT	Bare Pipe-Non-Scaffold
B	UT	IRR-Non-Scaffold
C	UT	Bare Pipe-Scaffold
D	UT	Scaffold/IRR
E	UT	IRR Outage/T/A/CFT-0
F	UT	Scaffold IRR Outage T/A/CFT-0
G	RT	Non-Scaffold
H	RT	Scaffold
I	RT	Non-Scaffold SCAR
J	RT	Scaffold SCAR

Line Tag-Method/IRR-Scaffold/Location/Correlative No.

REFERENCE DRAWINGS

P&ID : PD57D-A-6-2/4

PFD :

ISO'S : MT57-L-P2003-1
MT57-L-P2004-1
MT57-L-P2005-2/3

REVISIONS

No.	DATE	DESCRIPTION	BY	CHK	ENG	APP'D
5	25/03/06	DRAWING UPDATE	DC			

OWNERS CONDITIONS

THIS DRAWING OWNED BY SUNCOR ENERGY IS CONDITIONALLY LOANED TO

WHO BY RECEIVING IT HAS AGREED NOT TO REPRODUCE OR COPY IT IN WHOLE OR IN PART OR TO FURNISH INFORMATION FROM IT TO OTHERS, OR TO MAKE USE OF IT THAT IS, OR MAY BE INJURIOUS TO SUNCOR INC. AND TO RETURN IT UPON REQUEST.

LEGEND:
○ DENOTES ULTRASOUND TEST
⬡ DENOTES RADIOGRAPHIC TEST

NOTES
1. ALL DIMENSIONS, ELEV'S AND COORDINATES ARE APPROXIMATE.

DRAWING INFORMATION

TITLE
PLANT: 57
57E-2A/57E-2D

RBMI CIRCUIT No. 57-001G 1-2

REV. 5

ACUREN JOB # 272-J280794
REPORT # UT-BALJIN-2026-28

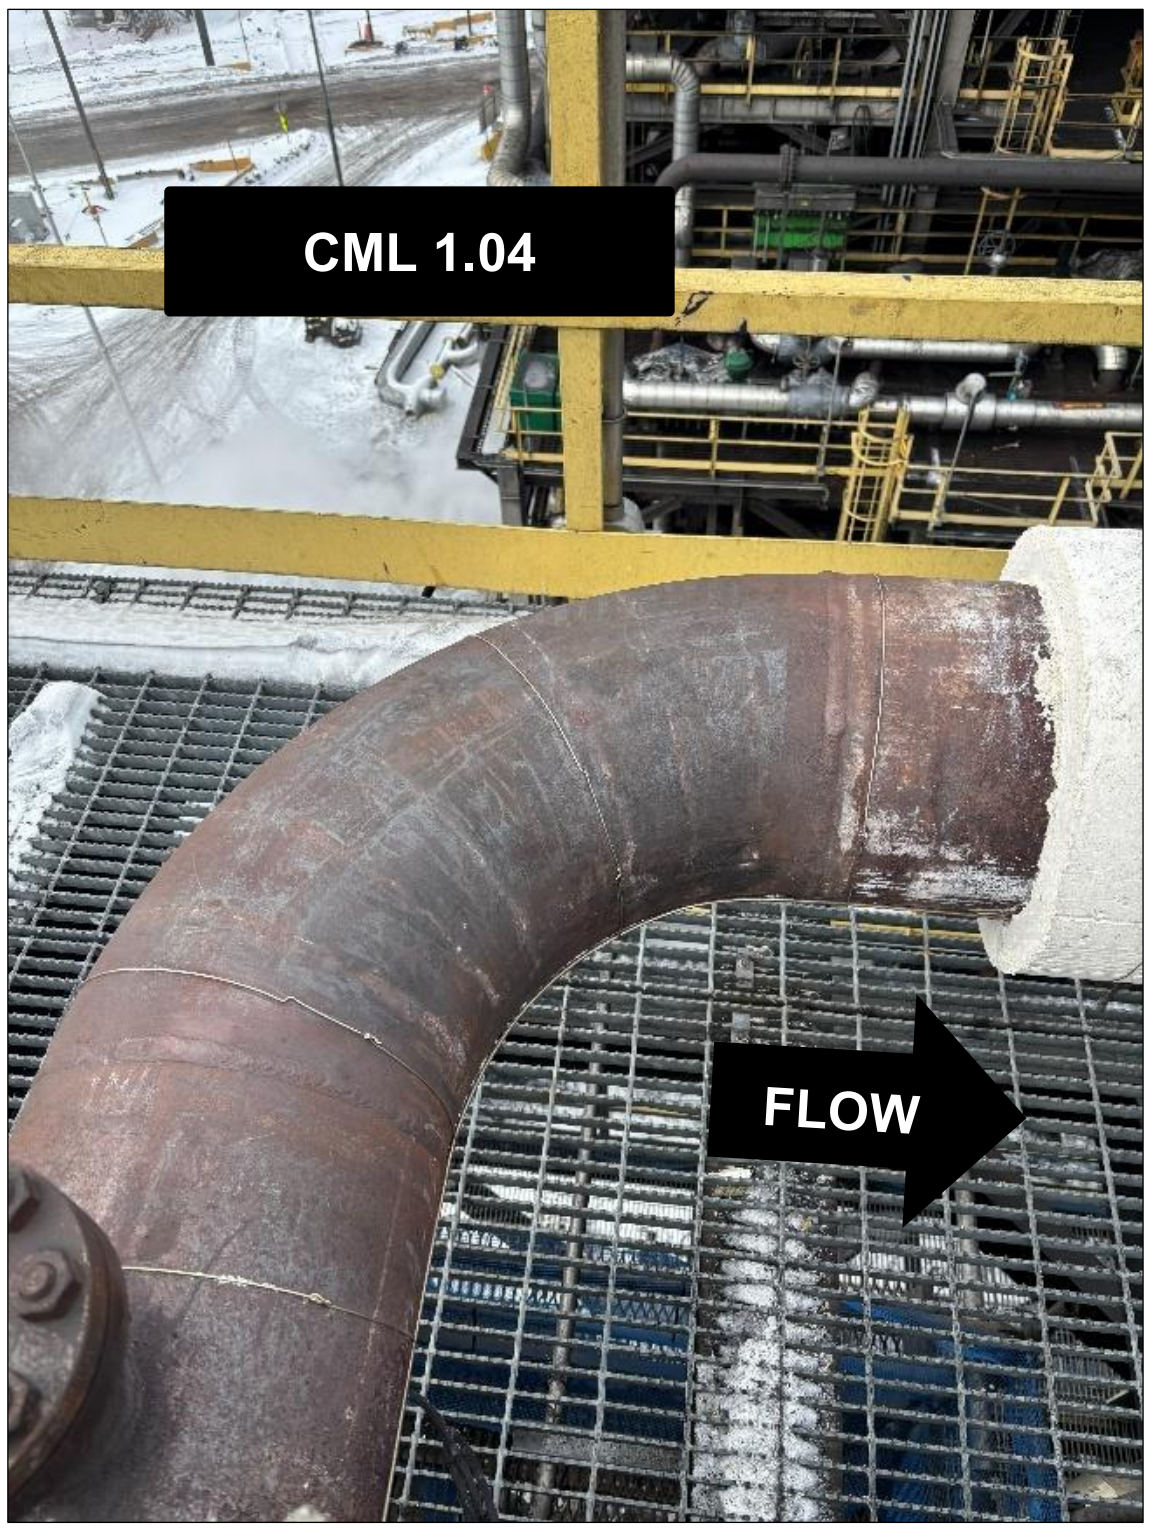

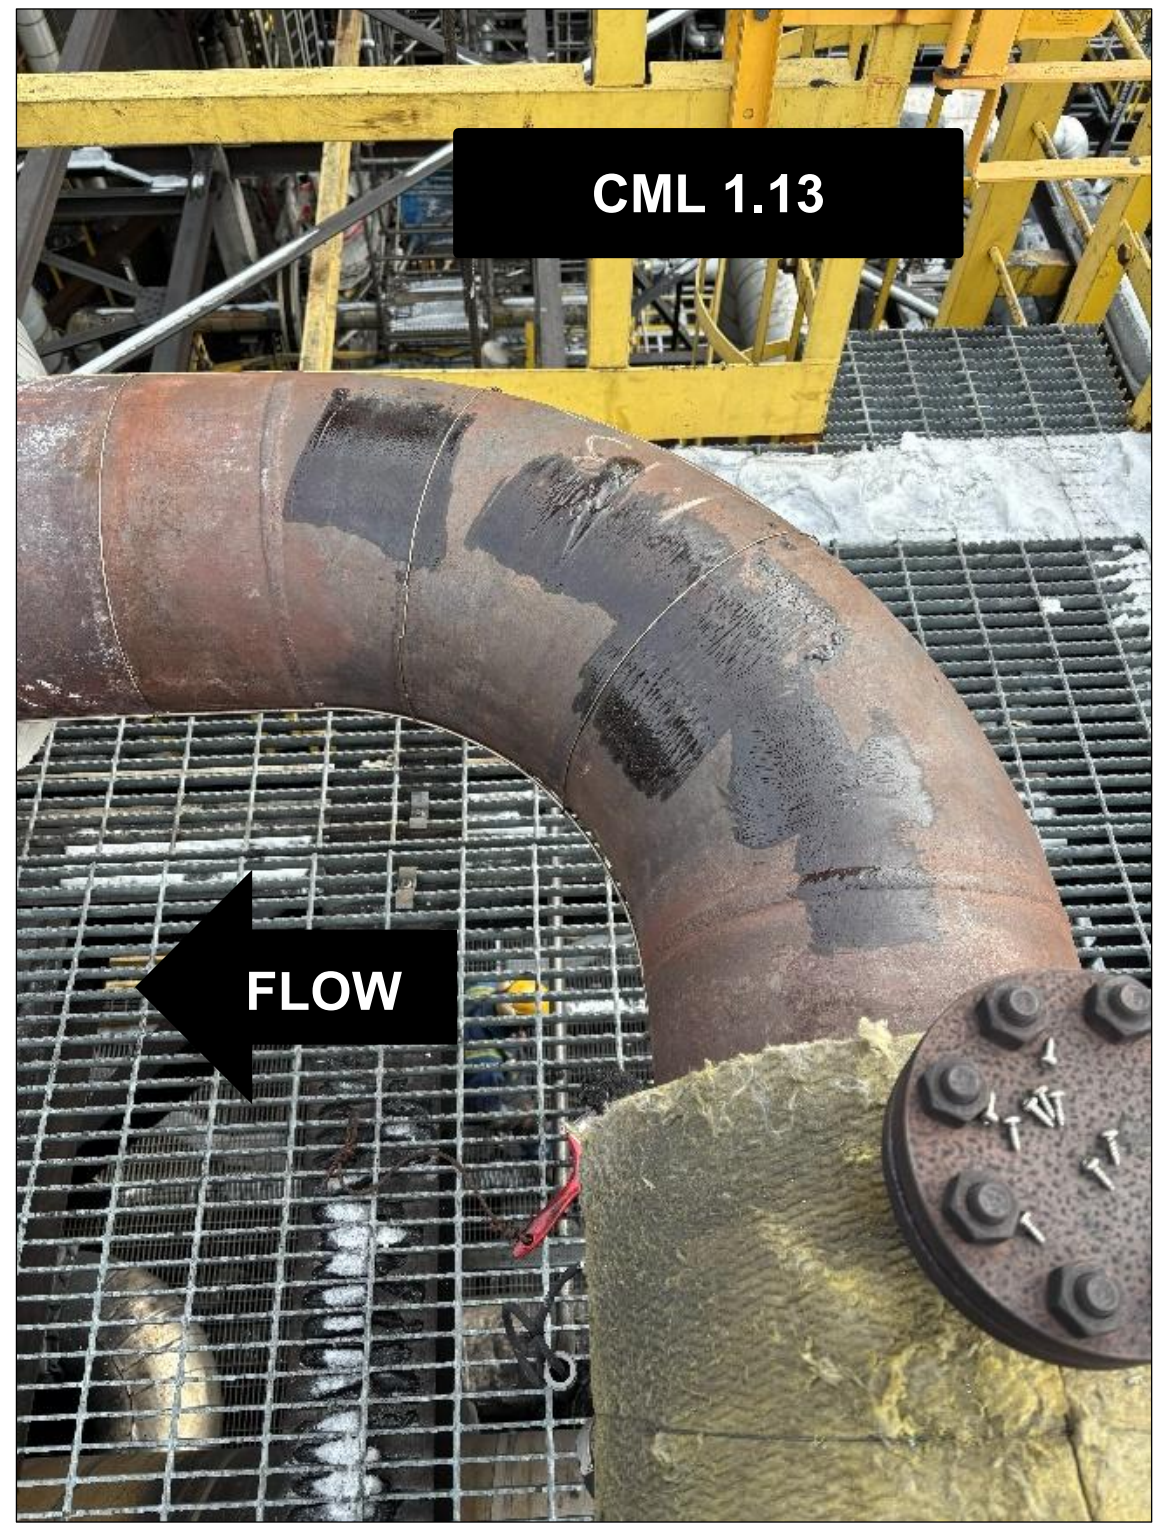

UT REPORT - ELBOW

SUNCOR ENERGY			
DATE (MM/DD/YYYY): 03/06/2026	METHOD:	Corrosion ☐	Erosion ☑
COMPANY: ACUREN	MATERIAL:	Carbon Steel ☑	Stainless Steel ☐
TECHNICIAN: JINEIL BALLESTEROS	ADDITIONAL INFORMATION:	SURFACE TEMP 240°F & 262°F	
ASSISTANT:			

PORT HOLES - CORROSION

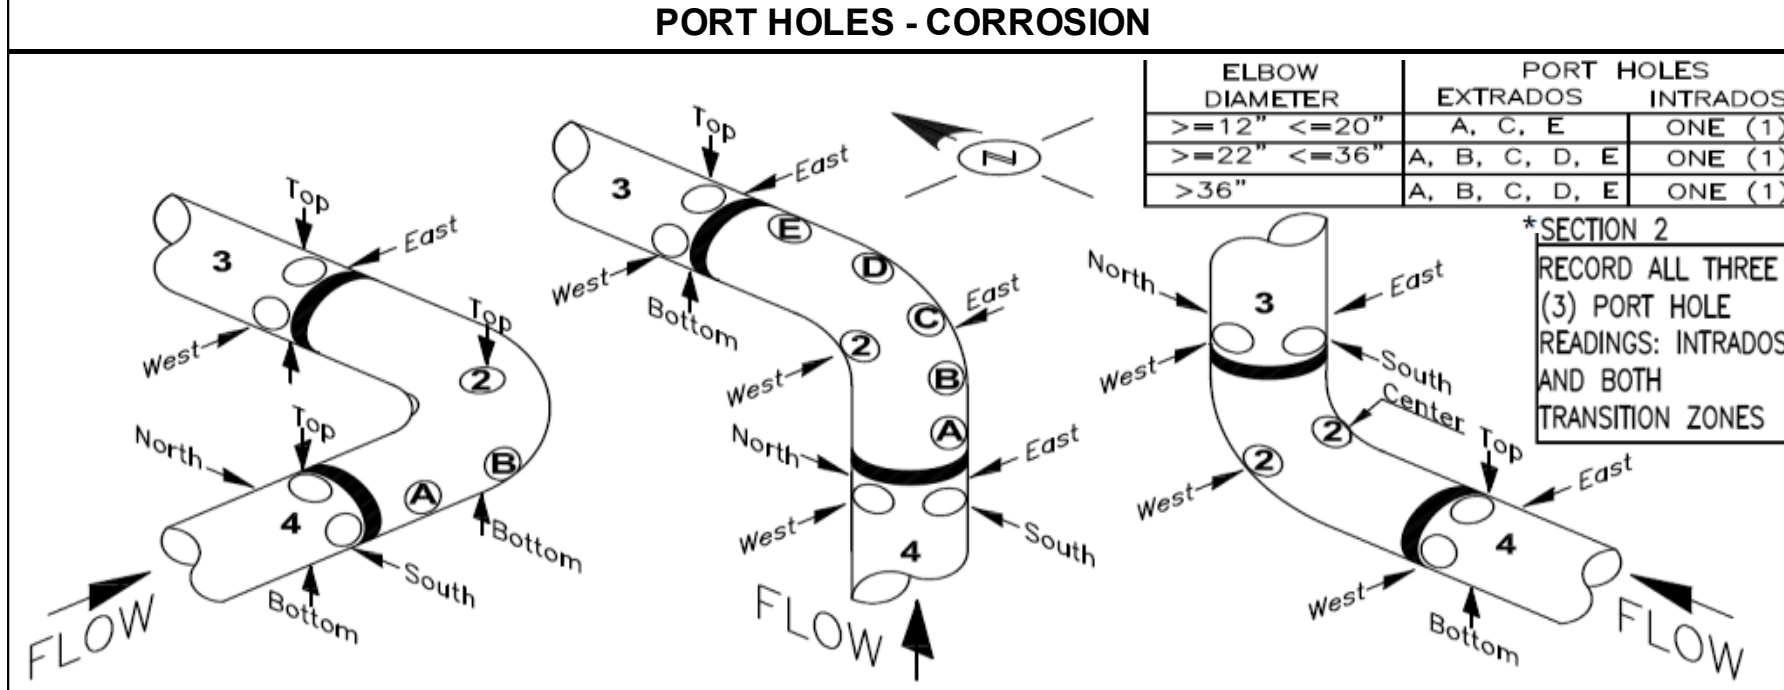

FULL SCAN - EROSION

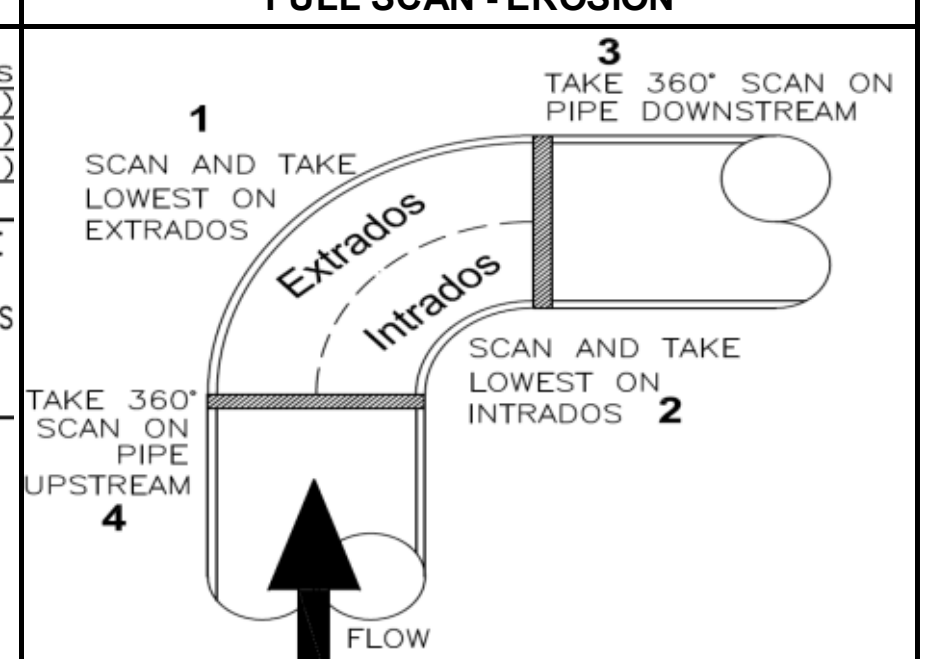

CIRCUIT	CML	SECTION	DIAM.	A	B	C	D	E	NORTH	SOUTH	EAST	WEST	TOP	BOTTOM	CENTER	HIGH	
57-001G 1-2	1.04	1	12"										0.385			0.433	
		2	12"											0.394		0.457	240°F
		3	12"										0.376			0.409	
		4	12"									0.377				0.412	
57-001G 1-2	1.13	1	12"									0.368				0.401	
		2	12"											0.356		0.451	262°F
		3	12"						0.385							0.415	
		4	12"										0.390			0.403	
